American Civil Constructors
MOUNTAIN WEST

Dos Rios GC

ID	Task Name	Duration	Start	Finish
1				
2	**Dos Rios Back Nine**	**37 days**	**Tue 9/5/23**	**Wed 10/25/23**
3	Mobilization	1 day	Tue 9/5/23	Tue 9/5/23
4	**Mainline**	**36 days**	**Wed 9/6/23**	**Wed 10/25/23**
5	10" Mainline	3 days	Wed 9/6/23	Fri 9/8/23
6	8" Mainline	8 days	Mon 9/11/23	Wed 9/20/23
7	6" Mainline	24 days	Thu 9/21/23	Tue 10/24/23
8	4" Mainline	1 day	Wed 10/25/23	Wed 10/25/23
9				
10	**Winter Shutdown**	**72 days?**	**Wed 11/22/23**	**Fri 3/1/24**
11		37 days?	Thu 11/23/23	Wed 11/22/23
12	**Dos Rios Back Nine Spring 2024**	**50 days**	**Mon 3/4/24**	**Fri 5/10/24**
13	**Laterals/ Heads**	**50 days**	**Mon 3/4/24**	**Fri 5/10/24**
14	Hole # 16	6 days	Mon 3/4/24	Mon 3/11/24
15	Hole # 14 & # 15	9 days	Tue 3/12/24	Fri 3/22/24
16	Hole # 13	10 days	Mon 3/25/24	Fri 4/5/24
17	Hole # 12	4 days	Mon 4/8/24	Thu 4/11/24
18	Hole # 17 & 11	11 days	Fri 4/12/24	Fri 4/26/24
19	Hole # 10 & # 18	10 days	Mon 4/29/24	Fri 5/10/24
20				
21	**Dos Rios Front Nine Spring 2024**	**107 days**	**Mon 3/4/24**	**Tue 7/30/24**
22	**Mainline**	**68 days**	**Mon 3/4/24**	**Wed 6/5/24**
23	10" Mainline	1 day	Mon 3/4/24	Mon 3/4/24
24	8" Mainline	8 days	Tue 3/5/24	Thu 3/14/24
25	6" Mainline	33 days	Fri 3/15/24	Tue 4/30/24
26	Mainline Bore	2 days	Wed 5/1/24	Thu 5/2/24
27	4" Mainline	24 days	Fri 5/3/24	Wed 6/5/24
28	**Laterals/ Heads**	**57 days**	**Mon 5/13/24**	**Tue 7/30/24**
29	Hole # 1	6 days	Mon 5/13/24	Mon 5/20/24
30	Hole # 3	6 days	Tue 5/21/24	Tue 5/28/24
31	Hole # 2	3 days	Wed 5/29/24	Fri 5/31/24
32	Hole # 8	5 days	Mon 6/3/24	Fri 6/7/24
33	Hole # 9	10 days	Mon 6/10/24	Fri 6/21/24
34	Hole # 7	2 days	Mon 6/24/24	Tue 6/25/24
35	Hole # 6	7 days	Wed 6/26/24	Thu 7/4/24
36	Hole # 5	7 days	Fri 7/5/24	Mon 7/15/24
37	Hole # 4	7 days	Tue 7/16/24	Wed 7/24/24
38	Driving Range	3 days	Thu 7/25/24	Mon 7/29/24
39	Putting Green	1 day	Tue 7/30/24	Tue 7/30/24

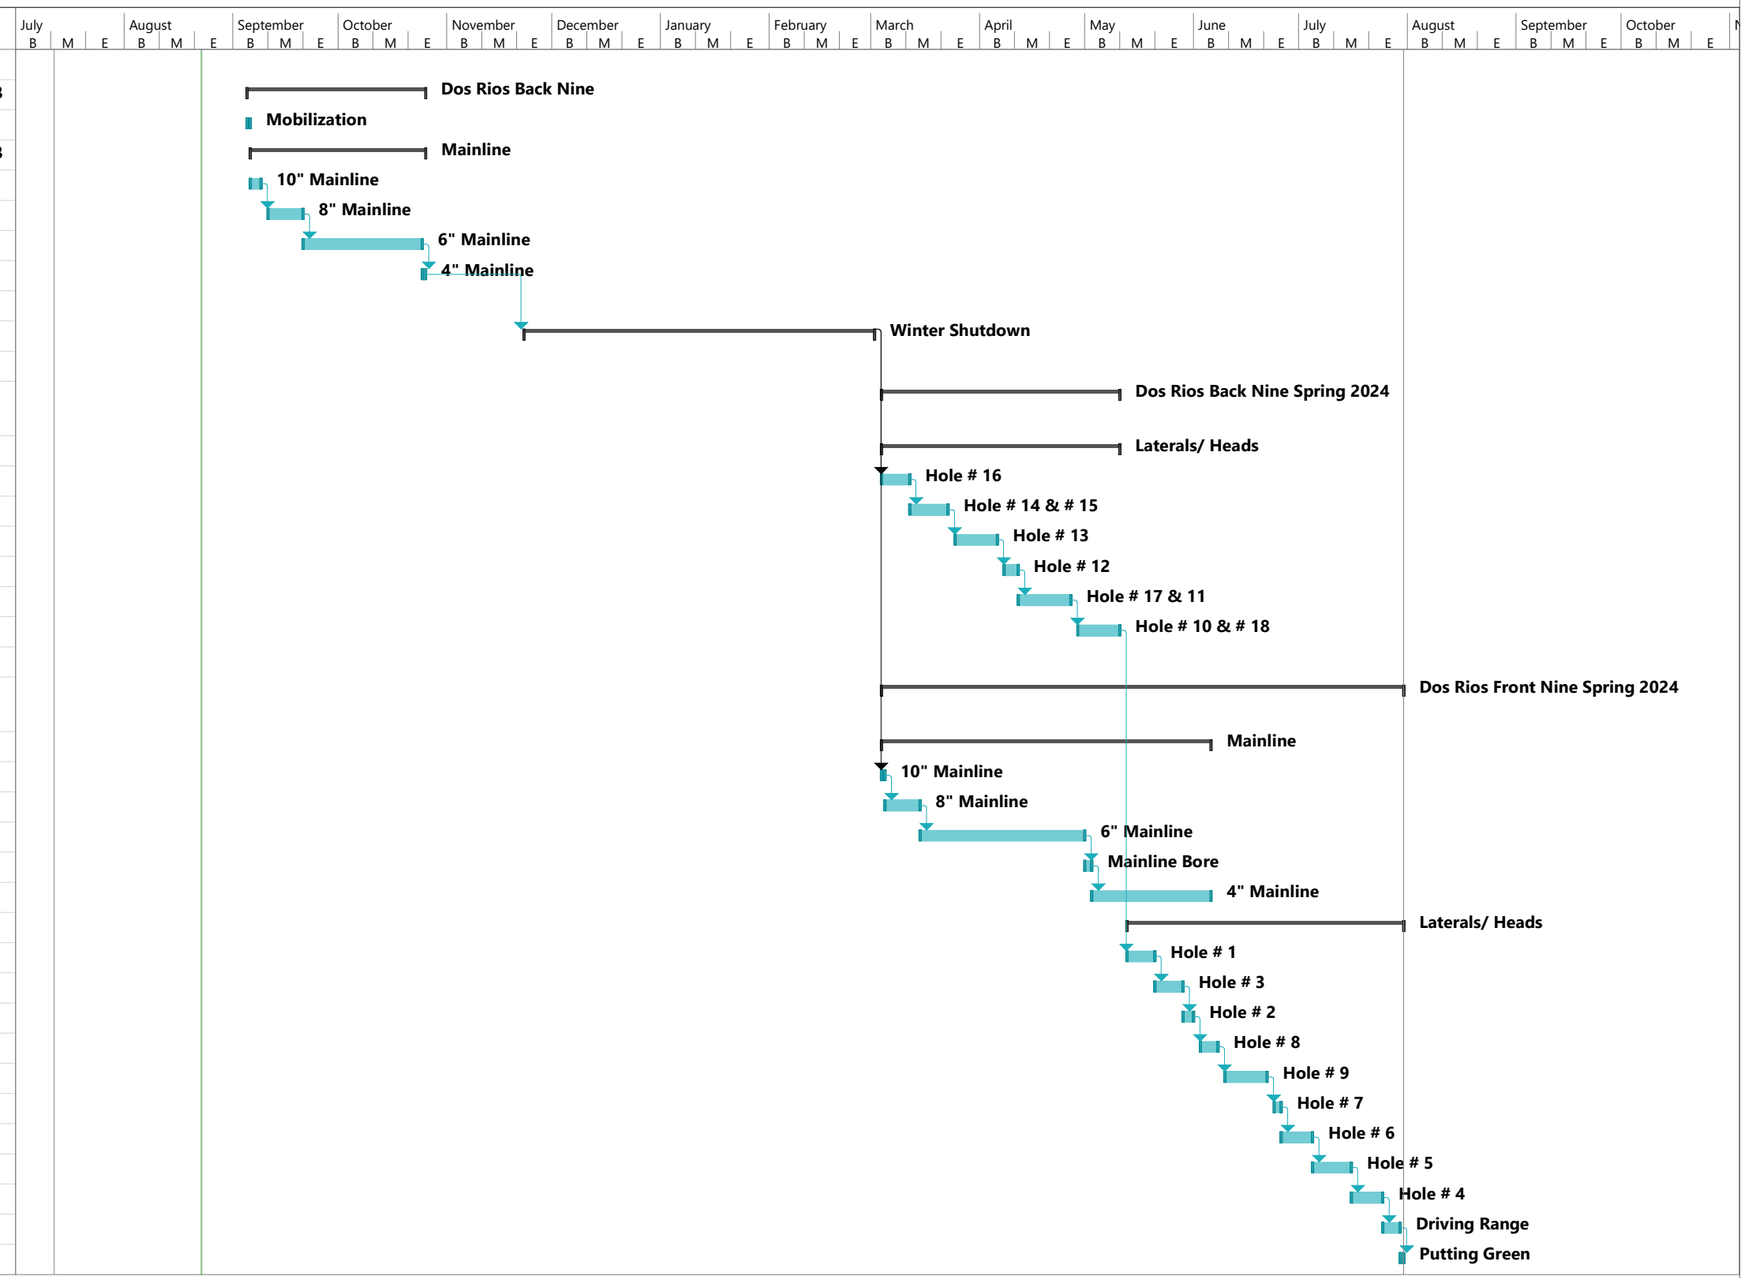

Project: 07-11-2023 Dos Rios S
Date: Wed 8/23/23

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Progress | Manual Progress
